


DEELGEBIEDEN EN TRANSPORTROUTES

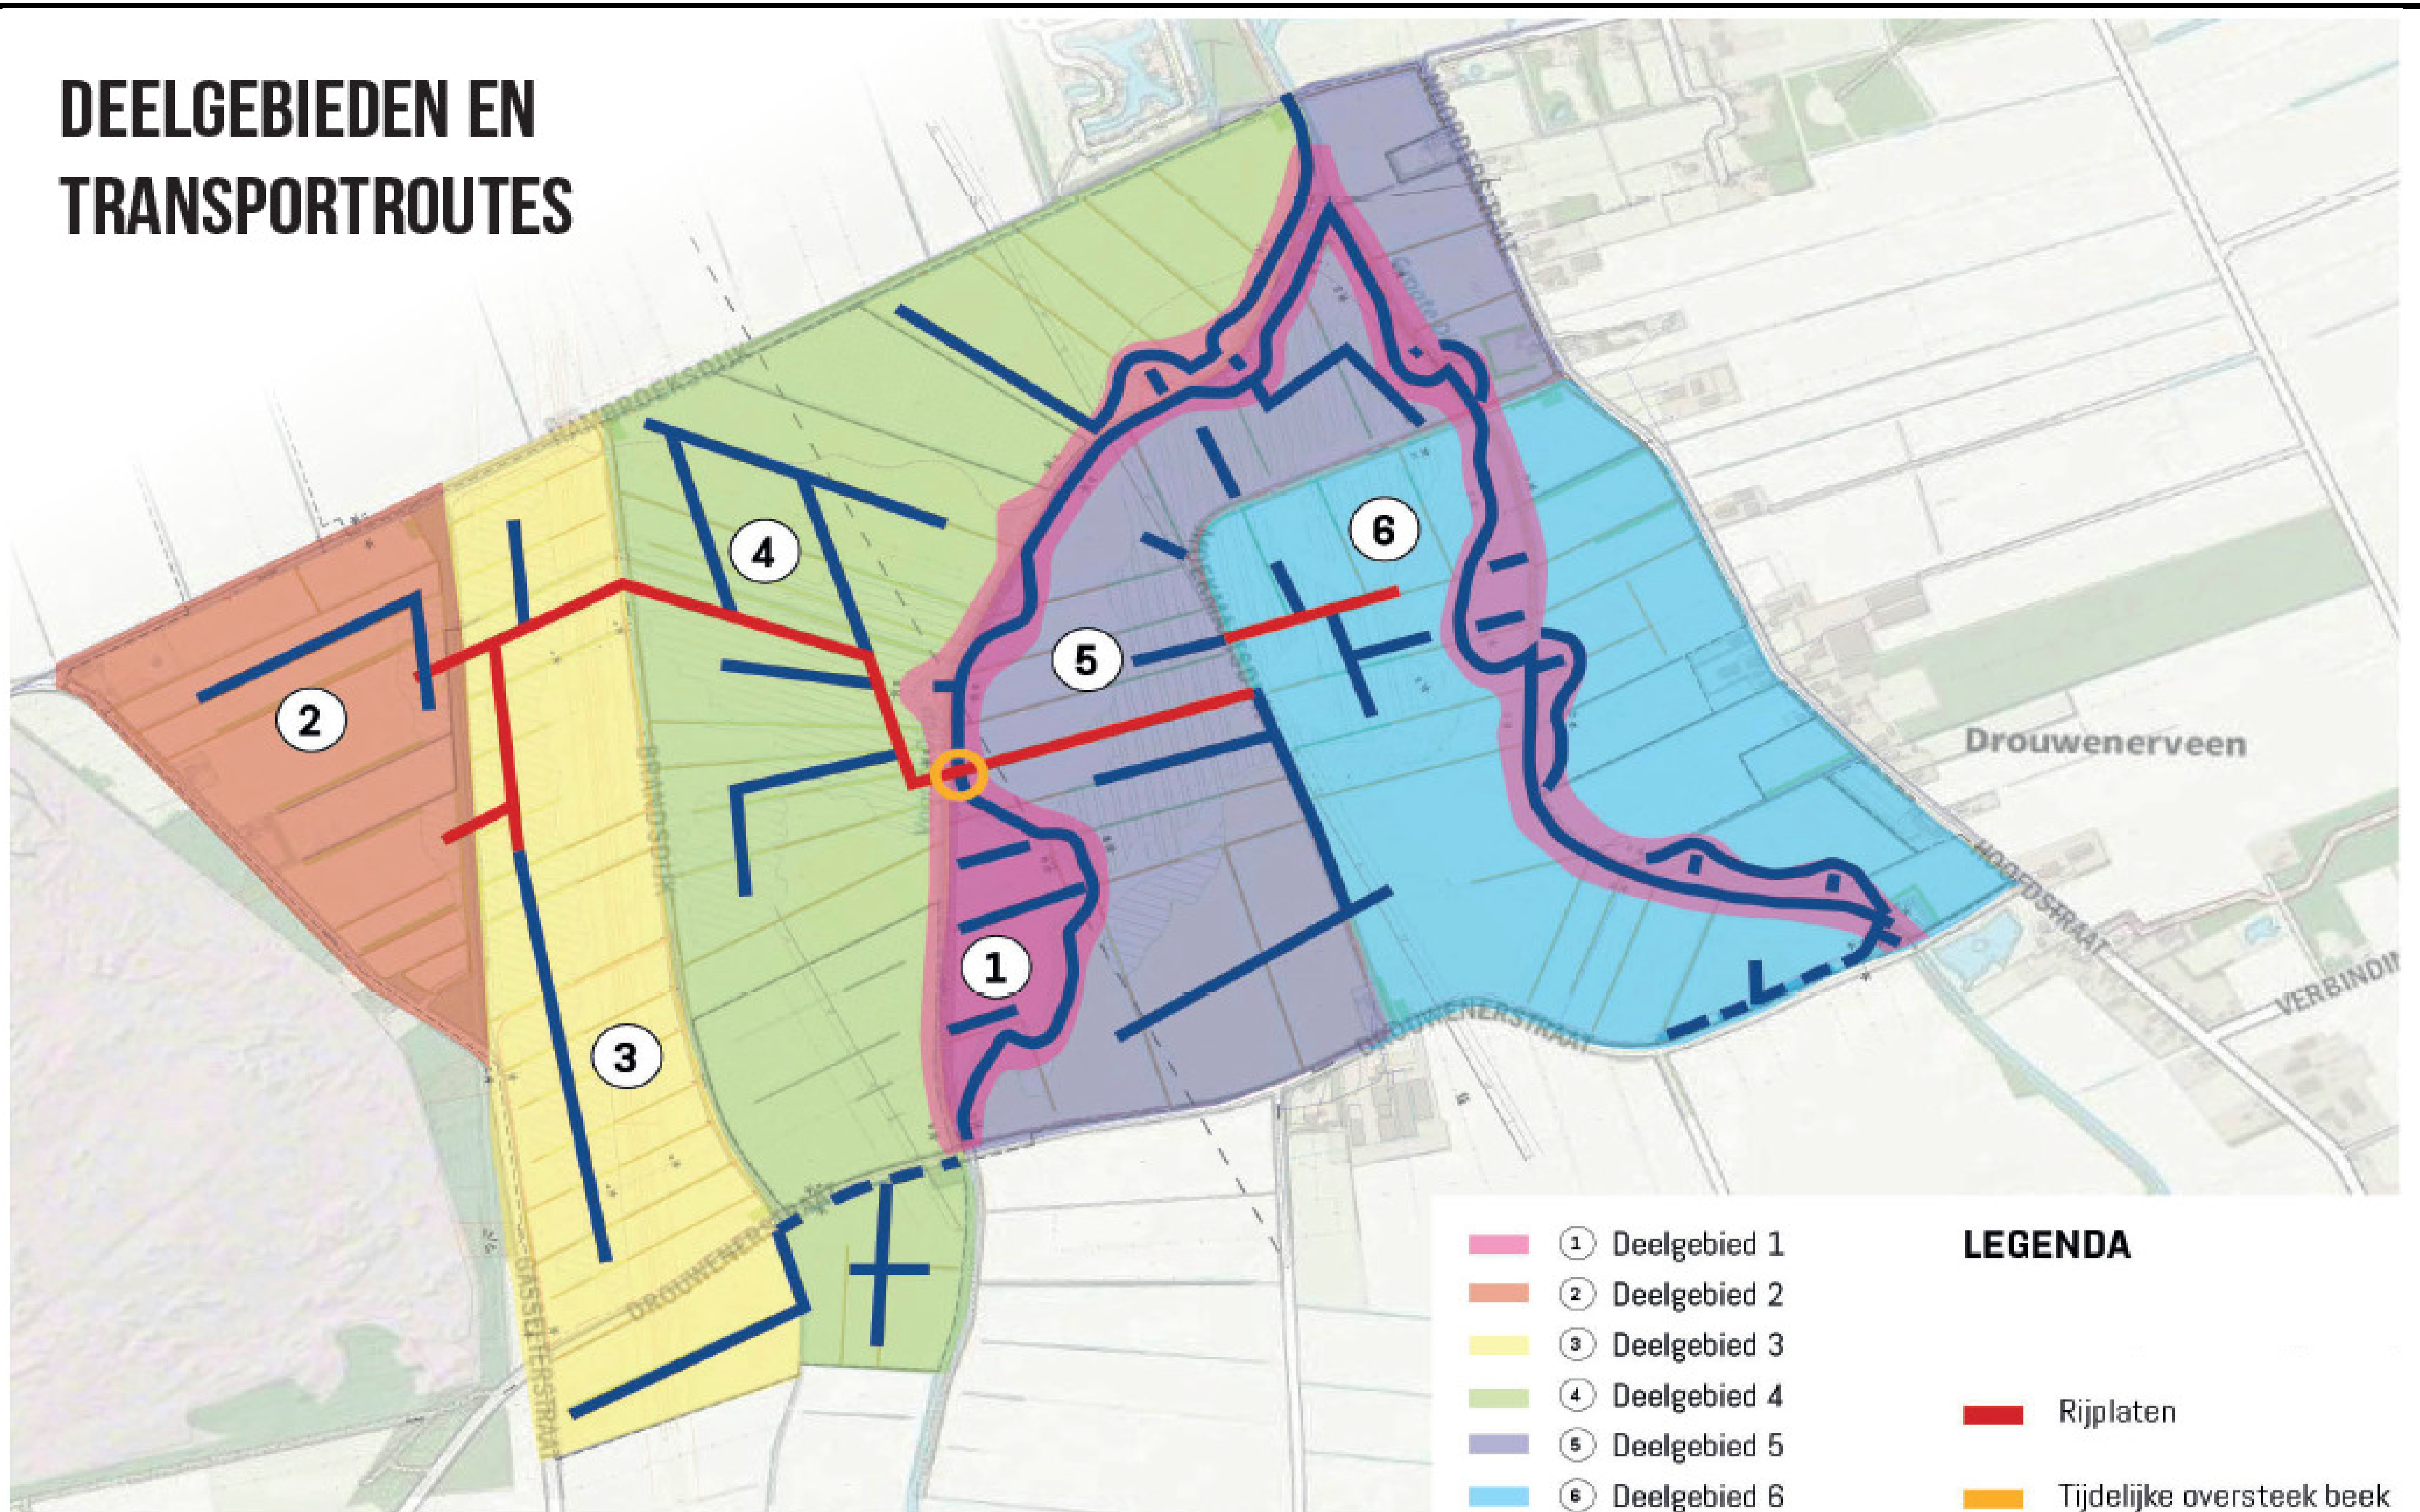

- LEGENDA**
- ① Deelgebied 1
 - ② Deelgebied 2
 - ③ Deelgebied 3
 - ④ Deelgebied 4
 - ⑤ Deelgebied 5
 - ⑥ Deelgebied 6
 - Rijplaten
 - Tijdelijke oversteek beek

WEEK	MAAND	DEELGEBIED 1	DEELGEBIED 2	DEELGEBIED 3	DEELGEBIED 4	DEELGEBIED 5	DEELGEBIED 6	
Week 14	April		Voorbereiding/kickoff	Voorbereiding/kickoff				
Week 15			Grondwerk					
Week 16				Duikers	Grondwerk			
Week 17								
Week 18	Mei		Terreininrichting	Duikers				
Week 19		Voorbereiding/kickoff		Fietspad	Voorbereiding/kickoff			
Week 20				Terreininrichting				
Week 21								
Week 22	Juni					Voorbereiding/kickoff		
Week 23								
Week 24						Grondwerk		
Week 25		Grondwerk						
Week 26								
Week 27	Juli					Grondwerk		
Week 28								
Week 29								
Week 30	Augustus				Duikers		Voorbereiding/kickoff	
Week 31						Duikers	Aanbrengen brug 1	
Week 32					Terreininrichting	Duikers K&L		Grondwerk
Week 33								
Week 34							Duikers	
Week 35							Moekmaatsdijk	
Week 36	September							
Week 37							Aanbrengen brug 2	
Week 38						Vispassage		
Week 39								
Week 40	Oktober							
Week 41						Terreininrichting	Vispassage	
Week 42								
Week 43								
Week 44		Oplevering waterhuishoudkundige werkzaamheden						
Week 45	November		Beplanting	Beplanting				
Week 46		Terreininrichting			Beplanting		Terreininrichting	
Week 47						Beplanting		
Week 48		Beplanting				Beplanting	Beplanting	
Week 49								
Week 50	December							
Week 51								
Week 52								
Week 1	Januari							
Week 2								
Week 3								
Week 4								
Week 5	Februari							
Week 6								
Week 7								
Week 8								
Week 9	Maart							
Week 10								
Week 11								
Week 12								
Week 13		Oplevering plant- en overige werkzaamheden						
